

# District Report

## Kathmandu Valley

16 – 22 February 2018

### Activity Summary

Activity	Contact Person	Reference Document
A field visit to Bungamati of Lalitpur Metropolitan City was conducted targeting the testing of the digitized forms for the surveys including Women's experience in Reconstruction, Temporary Shelter, and Community Reconstruction committee on 16 February 2018.	Sweata Sijapati <a href="mailto:techcord.ktm@hrrpnepal.org">techcord.ktm@hrrpnepal.org</a>	
Planning meeting for joint field monitoring visit of monitoring and evaluation consultant, MOUD-CLPIU and HRRP district technical team on 21 February 2018 at DUDBC hall, MOUD. The objective of the meeting was as follows: <ul style="list-style-type: none"> <li>To discuss the enhanced mechanism for joint field visits/monitoring visits in Districts</li> <li>For detail planning of one complete cycle of joint monitoring visit of Lalitpur, Bhaktapur and Kathmandu district.</li> <li>To plan for the meeting with representative of local bodies, municipality/rural municipality, POs, beneficiaries and personal involved in the reconstruction to discuss about the issue, challenges, good and bad practices in reconstruction.</li> </ul>	Sweata Sijapati <a href="mailto:techcord.ktm@hrrpnepal.org">techcord.ktm@hrrpnepal.org</a>	
Infopacks distributed to ward chief, ward secretary and engineers of Bungamati, Lalitpur Metropolitan City.	Sweata Sijapati <a href="mailto:techcord.ktm@hrrpnepal.org">techcord.ktm@hrrpnepal.org</a>	
Update of the contact list of Kathmandu, Lalitpur and Bhaktapur districts including the key focal person of the respective districts.	Sweata Sijapati <a href="mailto:techcord.ktm@hrrpnepal.org">techcord.ktm@hrrpnepal.org</a>	

### Upcoming Events & Meetings

Event / Meeting	Date, Time, and Location	Contact Person
Mason Training has been planned by DLPIU Lalitpur at Ikudol, Bagmati Rural Municipality.	23 Feb-1 March 2018 (11-17 Falgun 2074)	Smrita Pokhrel <a href="mailto:smrita.pokhrel@gmail.com">smrita.pokhrel@gmail.com</a>
General Coordination Meeting of NRA Kathmandu. (The meeting was rescheduled due to the Banda on 20 February 2018)	26 February 2018 (14 Falgun 2074) at NRA Kathmandu office, 12.30 PM	Ambika Amatya <a href="mailto:dc.ktm@hrrpnepal.org">dc.ktm@hrrpnepal.org</a>
HRRP survey on Temporary Shelter, Women in Reconstruction, and Community Reconstruction Committee (CRC) at Kathmandu, Lalitpur and Bhaktapur districts.	Feb 2018 – 15 March 2018	Sweata Sijapati <a href="mailto:techcord.ktm@hrrpnepal.org">techcord.ktm@hrrpnepal.org</a> Ambika Amatya <a href="mailto:dc.ktm@hrrpnepal.org">dc.ktm@hrrpnepal.org</a>
Interaction meeting of 'District Facilitation Committee', by involving key stakeholders of	26 February 2018 (14 Falgun 2074)	Goma Devi Dhakal NRA Lalitpur Chief

## Upcoming Events & Meetings

the districts such as municipalities, rural municipalities and district lines agencies.		<a href="mailto:nralalitpur@gmail.com">nralalitpur@gmail.com</a>
3 sets of Mason Training at Lalitpur Metropolitan City have been planned by DLPIU Lalitpur. The list of the masons is being finalized.	End of February 2018	Smrita Pokhrel <a href="mailto:smrita.pokhrel@gmail.com">smrita.pokhrel@gmail.com</a>
To include details of upcoming events and meetings in the next bulletin, please share details with <a href="mailto:dc.ktm@hrrpnepal.org">dc.ktm@hrrpnepal.org</a> by COB Wednesday of each week.		

## News & Updates

### Reconstruction updates : Kathmandu district- Municipality Level

Municipality	Beneficiary no.	Grant Agreement	Reconstruction			1st Tranche	2nd tranche				3rd tranche				Grievance	
			Started	Completed	Self		Requested	Compliance	Non-Compliance	Ready for inspection	Requested	Compliance	Non-Compliance	Ready for inspection	Submitted	Addressed
Chandragiri	4921	4300	500	150	247	4230	376	276	2	65	298	117	2	42	1401	476
Shankharpur	5409	4741	653	185	120	4340	569	386	11	67	200	147		51	1045	748
Gokarneshwar	2631	2336	960	500	320	2296	978	320	480	500	386	165	106	142	1320	800
Dakshinkali	13331	3154	250		25	3002	235	215	6	17	80	70	3	10	915	630
Kirtipur	2869	2332	552	200		2109	508	452	24	21	378	306	39	33	1191	208
Kathmandu Metropolitan	7171	5500	800	57	90	5331	945	631	12		386	363	6		1108	
Tokha	1596	1491	330	50	330	1461	350	306	1	43	72	72	0	0	349	43
Budhanilkantha	2540	2049	680	200	375	1974	480	412	38	30	200	173	19	8	538	452
Tarkeshwor	5465	4025	852	0		3604	52	355	23	123	329	329	0	0	2493	162
Nagarjun	4699	3860	712	211	0	3413	683	652	0	36	211	195	0	12	873	531
Kageshwori Manahara	3216	3125	600	50	150	3039	700	477	15	150	150	88	2	62	771	771
<b>Total</b>	<b>53848</b>	<b>36913</b>	<b>6889</b>	<b>1603</b>	<b>1657</b>	<b>34799</b>	<b>5876</b>	<b>4482</b>	<b>612</b>	<b>1052</b>	<b>2690</b>	<b>2025</b>	<b>177</b>	<b>360</b>	<b>12004</b>	<b>4821</b>

## Field Visit Reports


Date	Location	Participants
16 February 2018	Bungamati Ward no. 23, Lalitpur Metropolitan City	<ul style="list-style-type: none"> <li>Anu Prasai Lama (National Coordination officer)</li> <li>Karishma Chand (Communication and Content Officer)</li> <li>Sushmita Dawadi (Communication and Content Officer)</li> <li>Monika Bajimaya (District Management Team- Information Manager)</li> <li>Deepak Saud (District Management Team- Technical Coordinator)</li> <li>Ruplal Aidi (Translator)</li> <li>Uttam Paudel (IM Manager)</li> <li>Rupa Panday (MEAL Coordinator)</li> <li>Ambika Amatya (District Coordinator- Kathmandu Valley)</li> <li>Sweata Sijapati (District Technical Coordinator- Kathmandu Valley)</li> </ul>

<b>Objective(s)</b>	<ul style="list-style-type: none"> <li>• Testing of the digitized forms for the surveys including Women's experience in Reconstruction, Temporary Shelter, and Community Reconstruction committee</li> <li>• Interaction with the ward chairman and technical person.</li> </ul>		
<b>Summary</b>	<p>HRRP national and district team jointly conducted a visit to Bungamati of Lalitpur Metropolitan City was conducted targeting the testing of the digitized forms for the surveys including Women's experience in Reconstruction, Temporary Shelter, and Community Reconstruction committee on 16 February. The major reason for selection of the area were:</p> <ul style="list-style-type: none"> <li>• An area within Lalitpur metropolitan city and only few kilometers away from the city centers people are still residing in temporary shelter.</li> <li>• Availability of the women beneficiaries</li> <li>• Bungamati reconstruction committee has been actively advocating for the preservation of the traditional reconstruction and cultural heritage of the area.</li> </ul> <p>As the part of the testing of the questionnaire survey 5 temporary shelter and 5 women in reconstruction especially women beneficiaries were interviewed. Along with the testing of the digitized form, an informal meeting with the Mr. Amir Shakya (Ward Chairman), Sagar Tuladhar (Ward member and Bungamati reconstruction committee) and Surendra Khadgi (Engineer) was conducted. As per the reconstruction update, the ward chairman informed that the bylaws has been passed for the area which addresses the 100% coverage of the land less than 1 anna and 90% coverage for up to 2 anna, uses of traditional practices such as brick in the front side and many more. The engineer of the area informed that building design of 52 houses has already been prepared and are in the phase of approval from the Lalitpur metropolitan.</p>		
<b>Challenges / Issues Identified</b>	<b>Action Required</b>	<b>Responsible</b>	<b>Timeframe</b>
The beneficiaries want to build their house but demolishing the damaged houses has been a problem. In the core area the house are in the area are joined to each other and demolishing one house might weaken the adjoining structure and create risk to be people residing in the house.	The issues needs to be sorted out between the neighbors and during the demolishing process, there should not be any effect to other families or houses.	Beneficiaries, Community groups, local bodies.	As soon as possible
The houses are usually on the top of hills which are usually weakened by the land mice. This might have made the land vulnerable especially during the rainy season.	Identification of the issue in the area by the monitoring team. Depending on the monitoring required action needs to be suggested.	M&E consultant, Local bodies	

**Photos**



Bungamati Ward no. 22, Lalitpur Metropolitan City, Temporary shelter constructed using the CGI sheets. The beneficiary has received the 1<sup>st</sup> tranche.

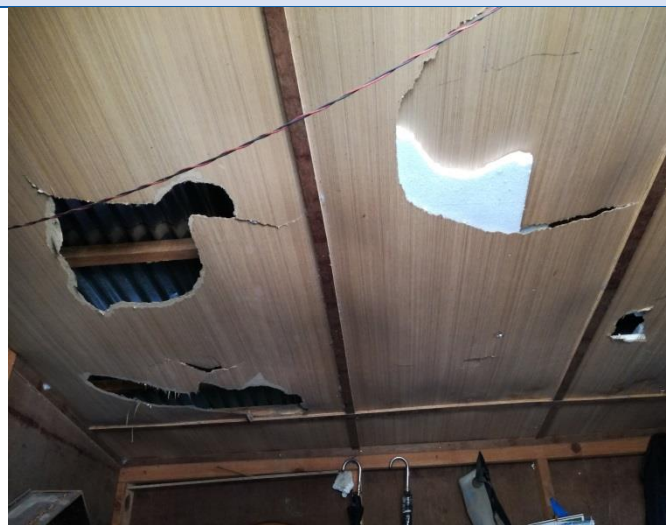

Bungamati Ward no. 22, Lalitpur Metropolitan City, the modification of temporary shelter constructed using wooden frames. The damaged roof has been fixed using the CGI sheets. The beneficiary of the house has received the 1<sup>st</sup> tranche.



Bungamati Ward no. 22, Lalitpur Metropolitan City, Temporary shelter constructed using the wooden frame and CGI roofing. The material for the temporary shelter has been supported from the Danish Aid. The beneficiary (Dhandevi Tuladhar) has received the 1<sup>st</sup> tranche.



Bungamati Ward no. 22, Lalitpur Metropolitan City, Mr. Ram Chandra Maharjan being interviewed by HRRP staff (Anu Prasai Lama) as a part of HRRP survey on reconstruction. The beneficiary has received 1<sup>st</sup> tranche and has built a load bearing structure along with the rainwater harvesting system.

**Questions Collected**

Question	Who Asked the Question?	Response Provided (By Whom)
What is the deadline for requesting the 2 <sup>nd</sup> tranche?	Beneficiary	The request for the second tranche must be made before the end of Chaitra 2074. (HRRP Staff)
The houses that are built before the government guidelines and inspection	Ward staff	For those under considered as non-compliance, engineers should be consulted to see if the houses can be addressed

## Questions Collected

<p>procedure are considered as non-compliance. How will those houses be eligible for the 2<sup>nd</sup> and 3<sup>rd</sup> tranches?</p>	<p>by the correction and exception manual or conduct the structural analysis of the structure and show that the structure is safe. Either of the options will make the house eligible for the tranche. (HRRP staff)</p>
--	---

## Challenges and Way Forward

Challenge	Way Forward
<p>Bungamati was under Karyabinayak Municipality but after the restructuring of the municipalities, the area lies within the Lalitpur Metropolitan which has affected in the implementation of the bylaws that was approved by the old municipality.</p>	<p>A meeting between the local elected representative and the official of the metropolitan should be conducted to address the issues and make necessary changes so that the reconstruction in the area can progress.</p>
<p>The beneficiaries have not been able to build their house due to some communities' issues such as adjoining houses, debris clearance.</p>	<p>Local elected representative should facilitate in solving such issues and encourage beneficiaries to reconstruct the house and request tranche before the government deadline.</p>
<p>Some of the houses constructed before the implementation of the bylaws are not as per the norms of heritage reconstruction.</p>	<p>Local elected representative should facilitate in solving such issues and make strict guidelines in the core area to follow the traditional reconstruction practices.</p>
